

FPT • AIX PROGRAM

AI Native for FA

2026 AI application framework

Working draft for framework review • 07/2026

CONTEXT

Where FA stands and what AIX must achieve

ALREADY EXISTS

People capability

The AI-native PM enablement program is already designed and running.

NEW MANDATE

AIX ownership

FA now needs a broader AI transformation plan, extending from people into delivery and customer-facing outcomes.

NOW REQUIRED

Plan to end-2026

Apply AI to internal delivery and customer value with measurable business outcomes.

Common scorecard: every initiative must be expressed through the FPT-style 6-Ro logic — problem, mission, deadline, result, owner, and budget.

Three AI pillars with one governance base



AI for Delivery

AI-in • internal

Use AI to improve delivery productivity across coding, testing, review, documentation, and PM operations.

Margin up



AI for Customer

AI-out • revenue

Turn AI into customer-facing features, offerings, and win-rate advantage.

Win rate up



AI for People

Enablement

Create the human operating capability needed to make A and B real at scale.

Foundation for A and B

Base layer: governance, policy, telemetry, security, tool/IP rules, and budget discipline. For the next six months, practical focus sits on A and B, enabled by C.

People enablement already in motion

The PM AI Bootcamp provides the operating capability base for the wider AIX plan.

200-300

PMs in scope

4

tracks: PM / BA / SA / Dev

~9 weeks

1 day + 4 weeks + 4 weeks

4 waves

cohort rollout approach

Phase 1 AI Mindset

CASAN, L0-L5, AI-first mindset

Phase 2 Hands-on

Assignments, telemetry, governance practice

Phase 3 Capstone

Working Customer Zero + Dev Book + viva

Hard graduation gates

1

Capability score across 6 pillars

2


Live working system

3

Viva defense

No graduation if one of the three gates is missing.

How Pillar C connects to AIX business outcomes

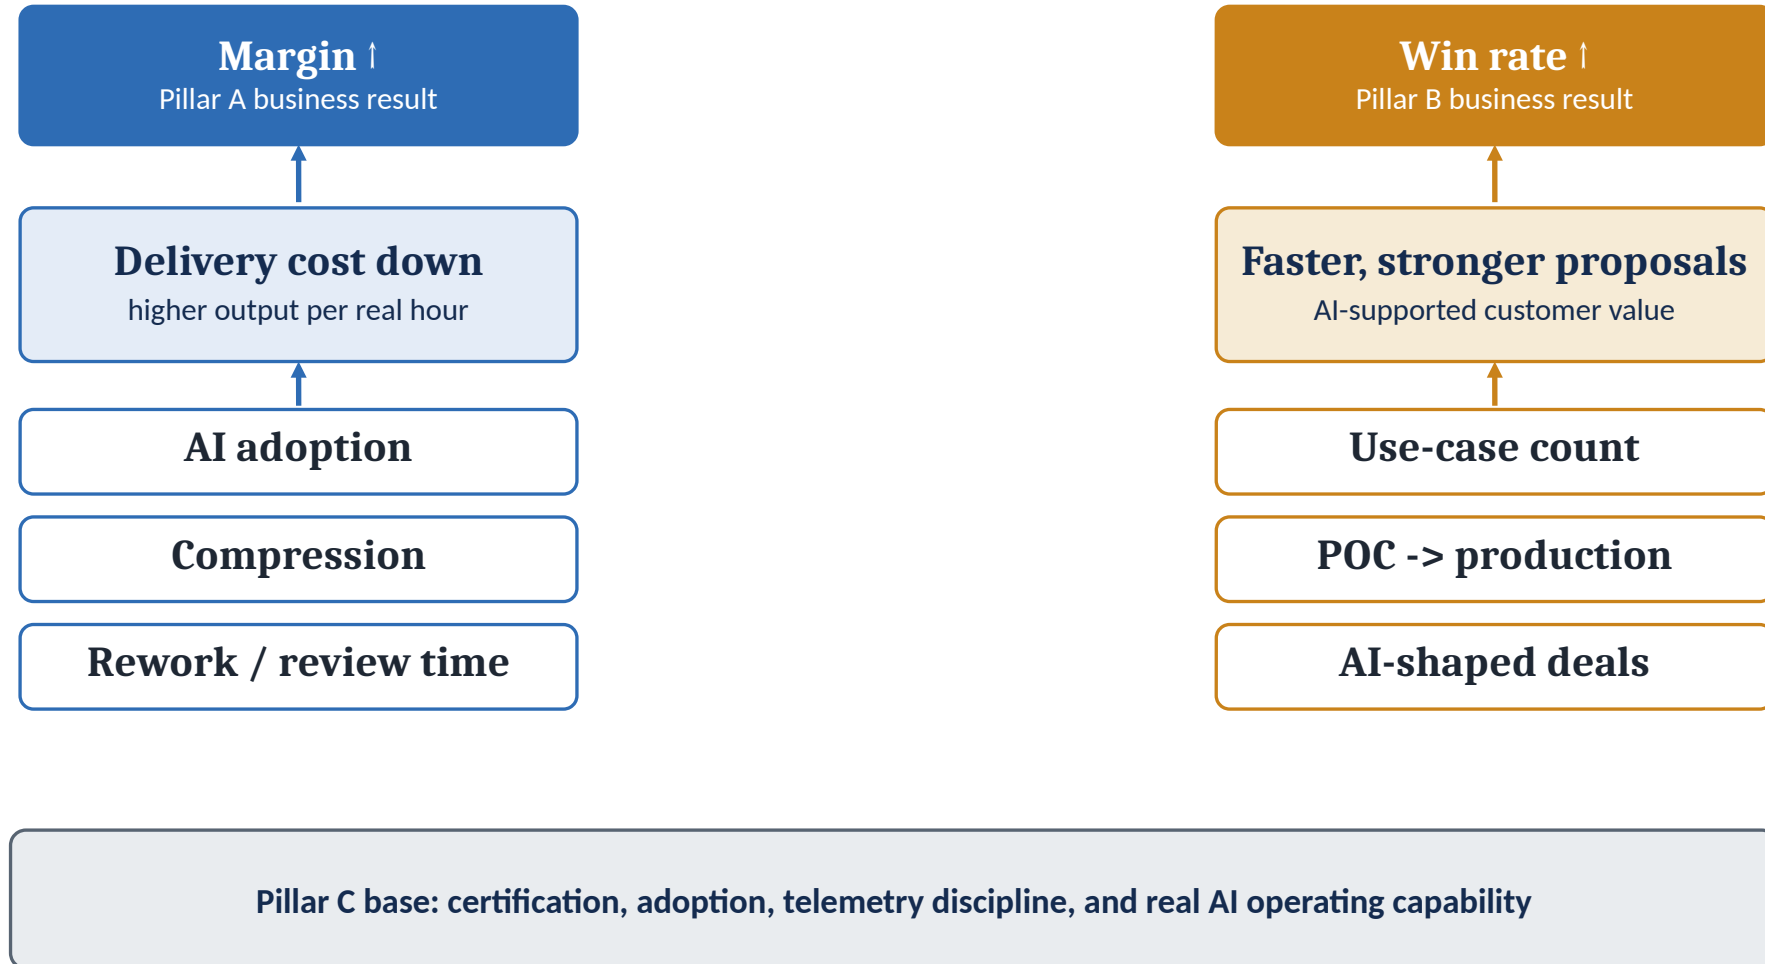

Q3-Q4 2026 priorities

	Q3 · 7-9/2026	Q4 · 10-12/2026
A · Delivery	Select and run pilot projects. Establish measurable delivery productivity cases.	Scale what works and turn it into repeatable playbooks or offerings.
B · Customer	Make AI visible in offer and proposal work where allowed.	Continue pushing customer-facing AI value and win-rate proof points.
C · People	Run early training batches and measure real adoption after training.	Continue later batches and build the champion community.
Governance	Publish policy, tool, IP, and dashboard rules.	Run mid-point review and end-of-year outcome review.

Operating principle: monthly progress reporting and quarterly outcome review.

NEXT STEP

What is still needed for a detailed plan

1

FA unit and domain scope

Need the exact FA context and domain focus to shape use-case selection.

2

Baseline numbers

Need rough current margin and win-rate baselines for attribution.

3

Q3-Q4 opportunity pipeline

Need known pilot accounts or proposal moments where AI can be tested.

4

Tool and budget assumptions

Need the practical boundary for licenses, governance, and specialist support.

Once these are fixed, the team can complete the KPI tree and fill the 6-Ro table for the 3-5 priority initiatives.
